


PROJECT MANAGEMENT



Presented by

Dr. BNV Siva Prasad

Assistant Professor

Department of Mining Engineering

Indian Institute of Technology (Banaras Hindu University), Varanasi

Former Scientist, National Institute of Rock Mechanics

sivaprasadbnv.min@itbhu.ac.in ; +91 77268 11680




Content

Project Planning

- Scope and significance
- Life Cycle
- Planning Process

Project Planning

- Project planning is the process of defining project goals, tasks, timelines, and resources to ensure successful project execution and delivery.

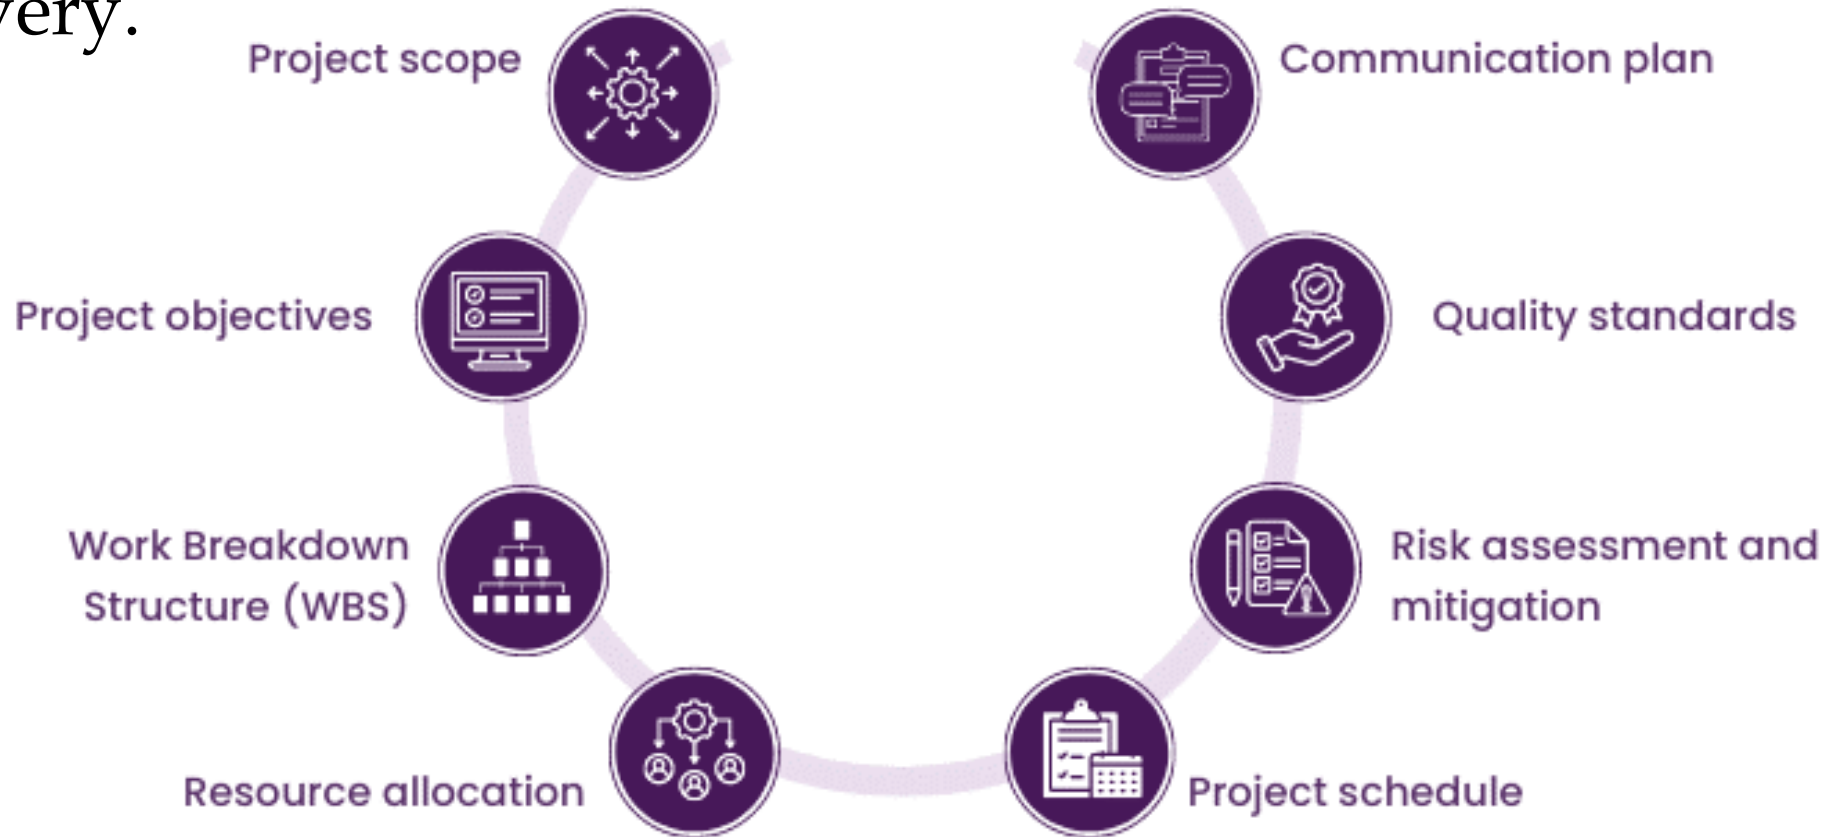

Key Components

Elements of Project Planning

- Project planning is a crucial phase in project management that involves outlining the steps necessary to achieve specific project objectives.
- It serves as a roadmap for the project team, detailing what needs to be done, when, and by whom.

Goals and Objectives

- Clearly defined outcomes that the project aims to achieve.

Tasks and Milestones

- Specific actions required to reach the project goals, along with key milestones to track progress.

Timeline

- A schedule that outlines when tasks will be completed and milestones reached.

Resources

- Identification of the necessary resources, including personnel, budget, and materials, to execute the project successfully.


Scope

- The scope of a project is a set of boundaries for the project within which there are defined goals the project is progressing towards.
- Beginning the project with a properly planned scope of the project ensures all the project goals and objectives are accomplished without any delays.
- The project scope is a detailed outline that describes all aspects of the project such as who are the key stakeholders, what are the project's resources, timelines, deliverables and other project-related activities. It explains all the processes and answers questions such as what the project is about or what is or is not included in it.

Scope

- Besides the project scope, there is also a **product scope**. There are several differences between them, and they should not be confused.
- **Product scope**: It describes the work performed to deliver a product, service, or result.
- The term “project scope” itself can sometimes imply the inclusion of product scope as a part of it.
- The product scope should be in a separate statement from the project scope statement, but both should be used to establish a clear understanding of what the project aims to achieve.
- **Product scope defines the features and functions of the project deliverables.**

Project Scope Management

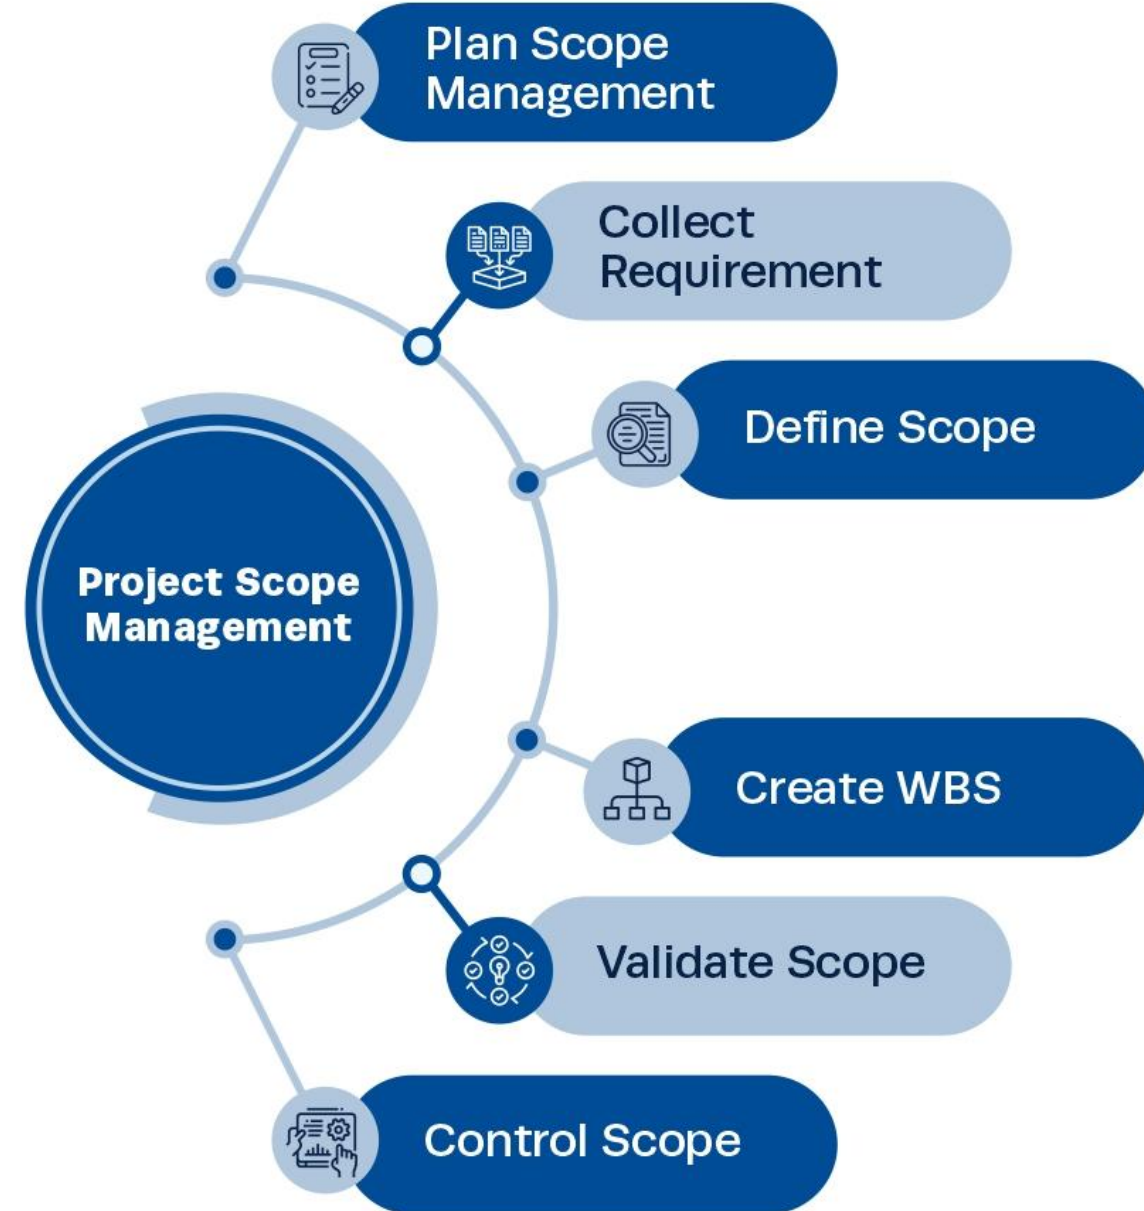

Project Scope Template

The project management scope statement, otherwise known as a scope document, usually consists of the following elements:

- **Introduction**
 - The introduction provides an overview of the entire project. It is a detailed breakdown of all of the tasks that the project team will perform, and it contains any important elements that might impact the outcome.
- **Project Scope**
 - This element is sort of the "main" part to define the project scope statement. The project scope should explain what the project does and does not include, helping managers avoid any confusion from project team members and stakeholders.
- **Exclusions**
 - Scope exclusions should also be stated. Exclusions can be anything that is not going to be a part of the project or its results. This refers to everything that is not factored in while planning the project.
- **Deliverables**
 - Deliverables are measurable outcomes indicating successful completion of the project. This part of the project scope statement should also include milestones and the exact due date of deliverables.
- **Constraints**
 - Constraints are describing possible limits of the project that might have a negative impact on its outcome. They can include resources, budget, timing, lack of information, etc.
- **Acceptance Criteria**
 - Acceptance criteria is agreement of how the success of the project will be measured. Having a well-defined acceptance criteria is useful for making sure there is no scope creep.
- **Final Approval**
 - And lastly, there should be a final approval. In this element of the scope statement, the customer signs off on the scope statement, confirming that all parameters have been included and the document is complete and accurate.

Significance

Effective project planning is essential for several reasons:




Clarity and Direction

It provides a clear understanding of the project scope and objectives, ensuring all team members are aligned.




Resource Management

Helps in allocating resources efficiently, minimizing waste and optimizing productivity.



Risk Mitigation


Identifies potential risks and challenges early on, allowing for proactive measures to be taken.



Stakeholder Communication


Facilitates better communication with stakeholders by providing a structured overview of the project's progress and expectations.

Significance

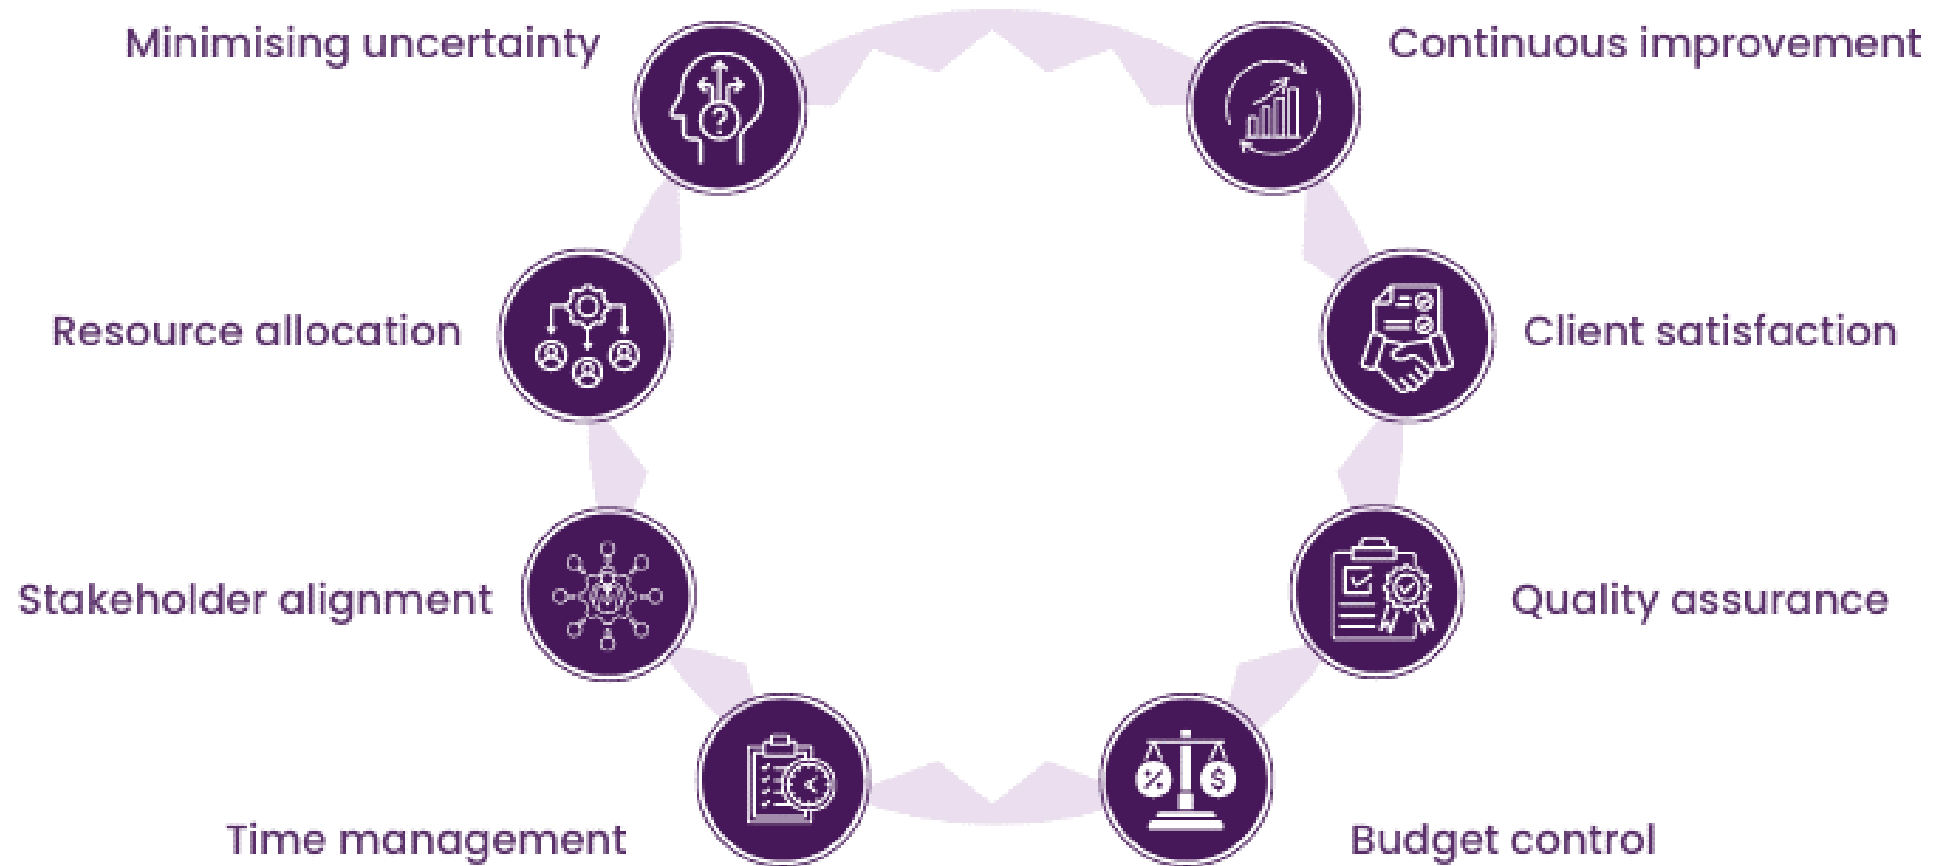

Project Life Cycle

- A Project life cycle is a structured framework that defines the phases a Project goes through, from initiation to completion.
- It typically includes stages like initiation, planning, execution, monitoring and controlling, and closure.
- Each phase has specific goals and tasks, ensuring organised and efficient Project Management.

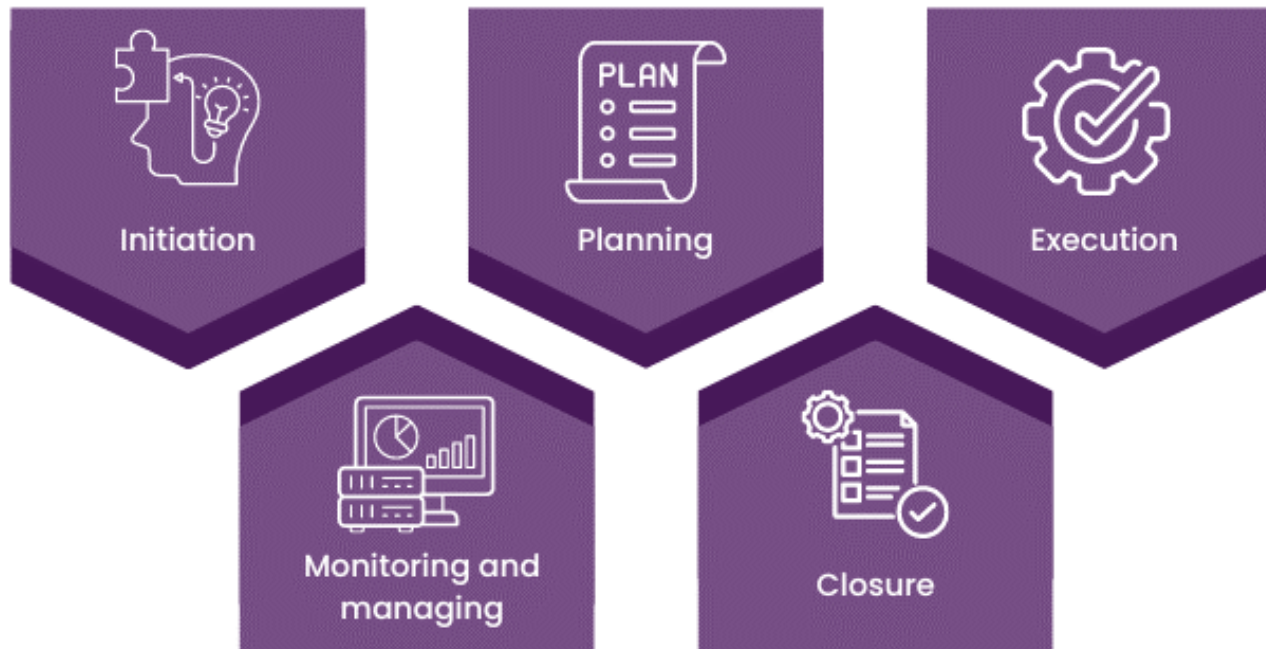

Key phases of Project Life Cycle


Steps in Project Planning

The project planning process typically involves the following steps:

Initiation	Define the project's purpose and scope, and obtain necessary approvals.
Planning	Develop a detailed project plan that includes tasks, timelines, and resource allocation.
Execution	Implement the project plan, ensuring that tasks are completed as scheduled.
Monitoring and Controlling	Track progress against the plan, making adjustments as necessary to stay on course.
Closure	Complete the project, review outcomes, and document lessons learned for future projects.

Project Planning - Tools

Effective Project Planning is crucial for business success, and having the right tools can greatly enhance the process.

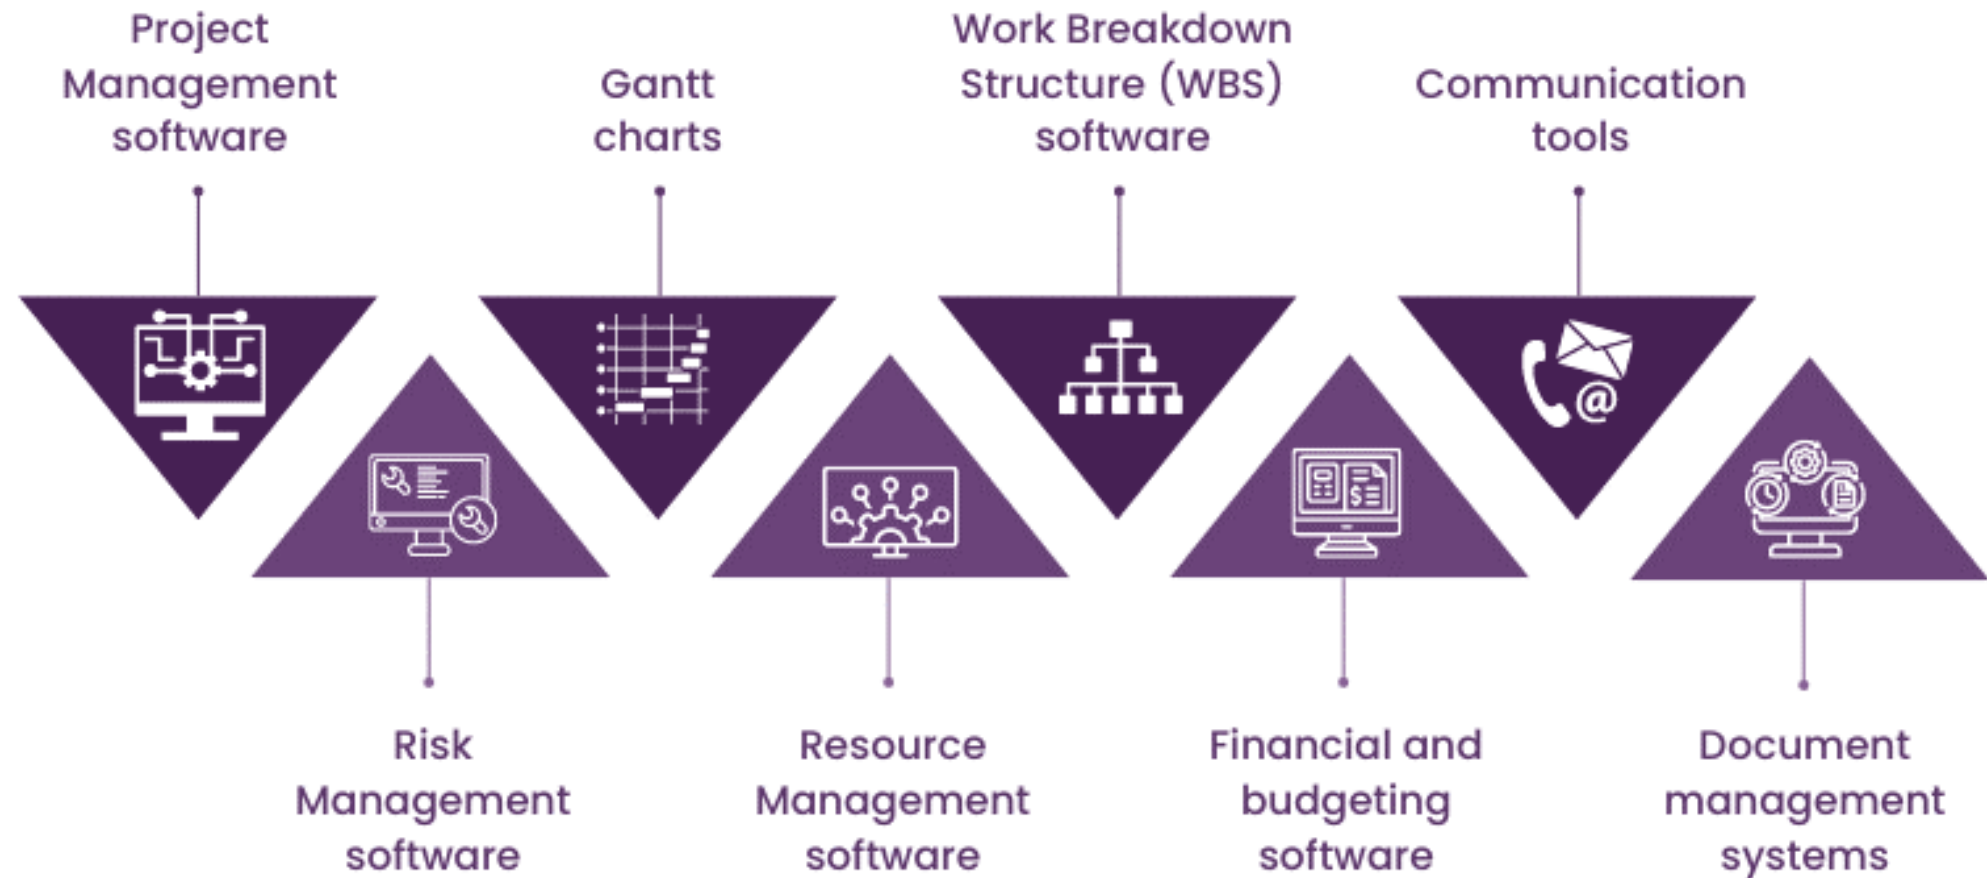

Key tools that businesses need for Project Planning

Project Planning - Tools

By following a structured approach to project planning, teams can enhance their chances of delivering successful projects on time and within budget.

Various tools and software can assist in project planning, including:



- A project management tool that helps teams organize tasks and track progress.



- A visual tool for managing projects and tasks using boards and cards.



- A comprehensive project management software that offers advanced planning and scheduling features.



- Primarily used for software development projects, it helps teams plan, track, and manage agile projects.

References

- [Essentials of Project Management by ADAM FARAG](#)
- [The Handbook of Project Management by Martina Huemann and Rodney Turner](#)
- <https://instituteprojectmanagement.com/blog/successful-project-manager-iv-project-scope-planning-2/#:~:text=Project%20scope%20defines%20the%20boundaries%20and%20goals%20of,is%20a%20crucial%20step%20for%20successful%20project%20execution.>
- <https://www.theknowledgeacademy.com/blog/importance-of-project-planning/>



Thank You

Any Queries ???

Contact

sivaprasadbnv.min@itbhu.ac.in

+91 77268 11680
